



**ALMA Task Scheduling**  
Antenna Testing selected


ID	WBS (f)	Task	Start	Finish	Duration	2002												J	F	M
						F	M	A	M	J	J	A	S	O	N	D				
46	9.7.2.1.4	Slew Rate Check	3/26/2002	3/26/2002	1d															
47	9.7.2.1.5	Tracking Check	3/16/2002	3/19/2002	4d															
48	9.7.2.1.6	Weather Proofing Check	3/19/2002	3/25/2002	7d															
49	9.7.2.1.7	AUI Equipment Installation and Removal Checks	3/23/2002	3/23/2002	1d															
50	9.7.2.1.8	Grounding Checks	3/27/2002	3/27/2002	1d															
51	9.7.2.1.9	Antenna "hard-stop" Motion Tests	3/24/2002	3/24/2002	1d															
52	9.7.2.1.10	Optics Check	3/25/2002	3/31/2002	7d															
53	9.7.2.1.11	Cable Wrap Tests	3/28/2002	3/29/2002	2d															
54	9.7.2.1.12	Transporter Interface	3/30/2002	3/30/2002	1d															
55	9.7.2.1.13	Safety Inspection	4/1/2002	4/2/2002	2d															
56	9.7.2.1.14	Surface Setting	4/3/2002	4/16/2002	14d															
<u>57</u>	<u>9.7.2.2</u>	<u>Dynamical/Mechanical Tests</u>	<u>4/17/2002</u>	<u>5/2/2002</u>	<u>15.5d</u>															
58	9.7.2.2.1	Tiltmeter Checks of AZ	4/17/2002	4/19/2002	3d															
59	9.7.2.2.2	Resonant Frequency Measurements	4/17/2002	4/17/2002	1d															
60	9.7.2.2.3	Acceleration Measurements	4/20/2002	4/21/2002	1d															
61	9.7.2.2.4	Movement Tests	4/21/2002	4/22/2002	1d															
62	9.7.2.2.5	Apex Translations	4/22/2002	4/23/2002	1d															
63	9.7.2.2.6	Optical Telescope Operation and Stability	4/20/2002	4/21/2002	1.5d															
64	9.7.2.2.7	Panel Mounting Stability	4/23/2002	4/26/2002	3d															
65	9.7.2.2.8	Transporter Testing of Antenna	4/21/2002	4/24/2002	3d															
66	9.7.2.2.9	Nutator Testing	4/17/2002	4/19/2002	3d															
67	9.7.2.2.10	Vertex Shutter	4/26/2002	4/29/2002	3d															
68	9.7.2.2.11	Receiver Cabin Temperature Stability and Capac	4/17/2002	4/20/2002	1d															
69	9.7.2.2.12	Calibration System Testing	4/17/2002	4/30/2002	14d															
70	9.7.2.2.13	Test Antenna Transporter Survival Conditions	4/24/2002	4/25/2002	1d															
71	9.7.2.2.14	Verify Code Compliance of Antenna	4/25/2002	4/26/2002	1d															
72	9.7.2.2.15	Test Antenna RFI/EMI	4/17/2002	4/19/2002	3d															
73	9.7.2.2.16	Verify Antenna Alignment	4/29/2002	5/2/2002	3d															
74	9.7.2.2.17	Evaluate Antenna Electrical Cooling at Altitude	4/26/2002	4/27/2002	1d															
75	9.7.2.2.18	Check Auto Stow, Emergency Stops, and Range	4/27/2002	4/28/2002	1d															
76	9.7.2.2.19	Evaluation of Antenna Manuals	4/28/2002	4/29/2002	1d															

Milestones: Summary Tasks: <b>bold type</b> <u>underline</u>	Joint Task 	Summary (Joint) 	Progress 	Summ. Progress 
	Eur Task 	Summary (Eur) 	Milestone 	Split 
	US Task 	Summary (US) 	Completed Mlstrn 	






**ALMA Task Scheduling**  
Antenna Testing selected

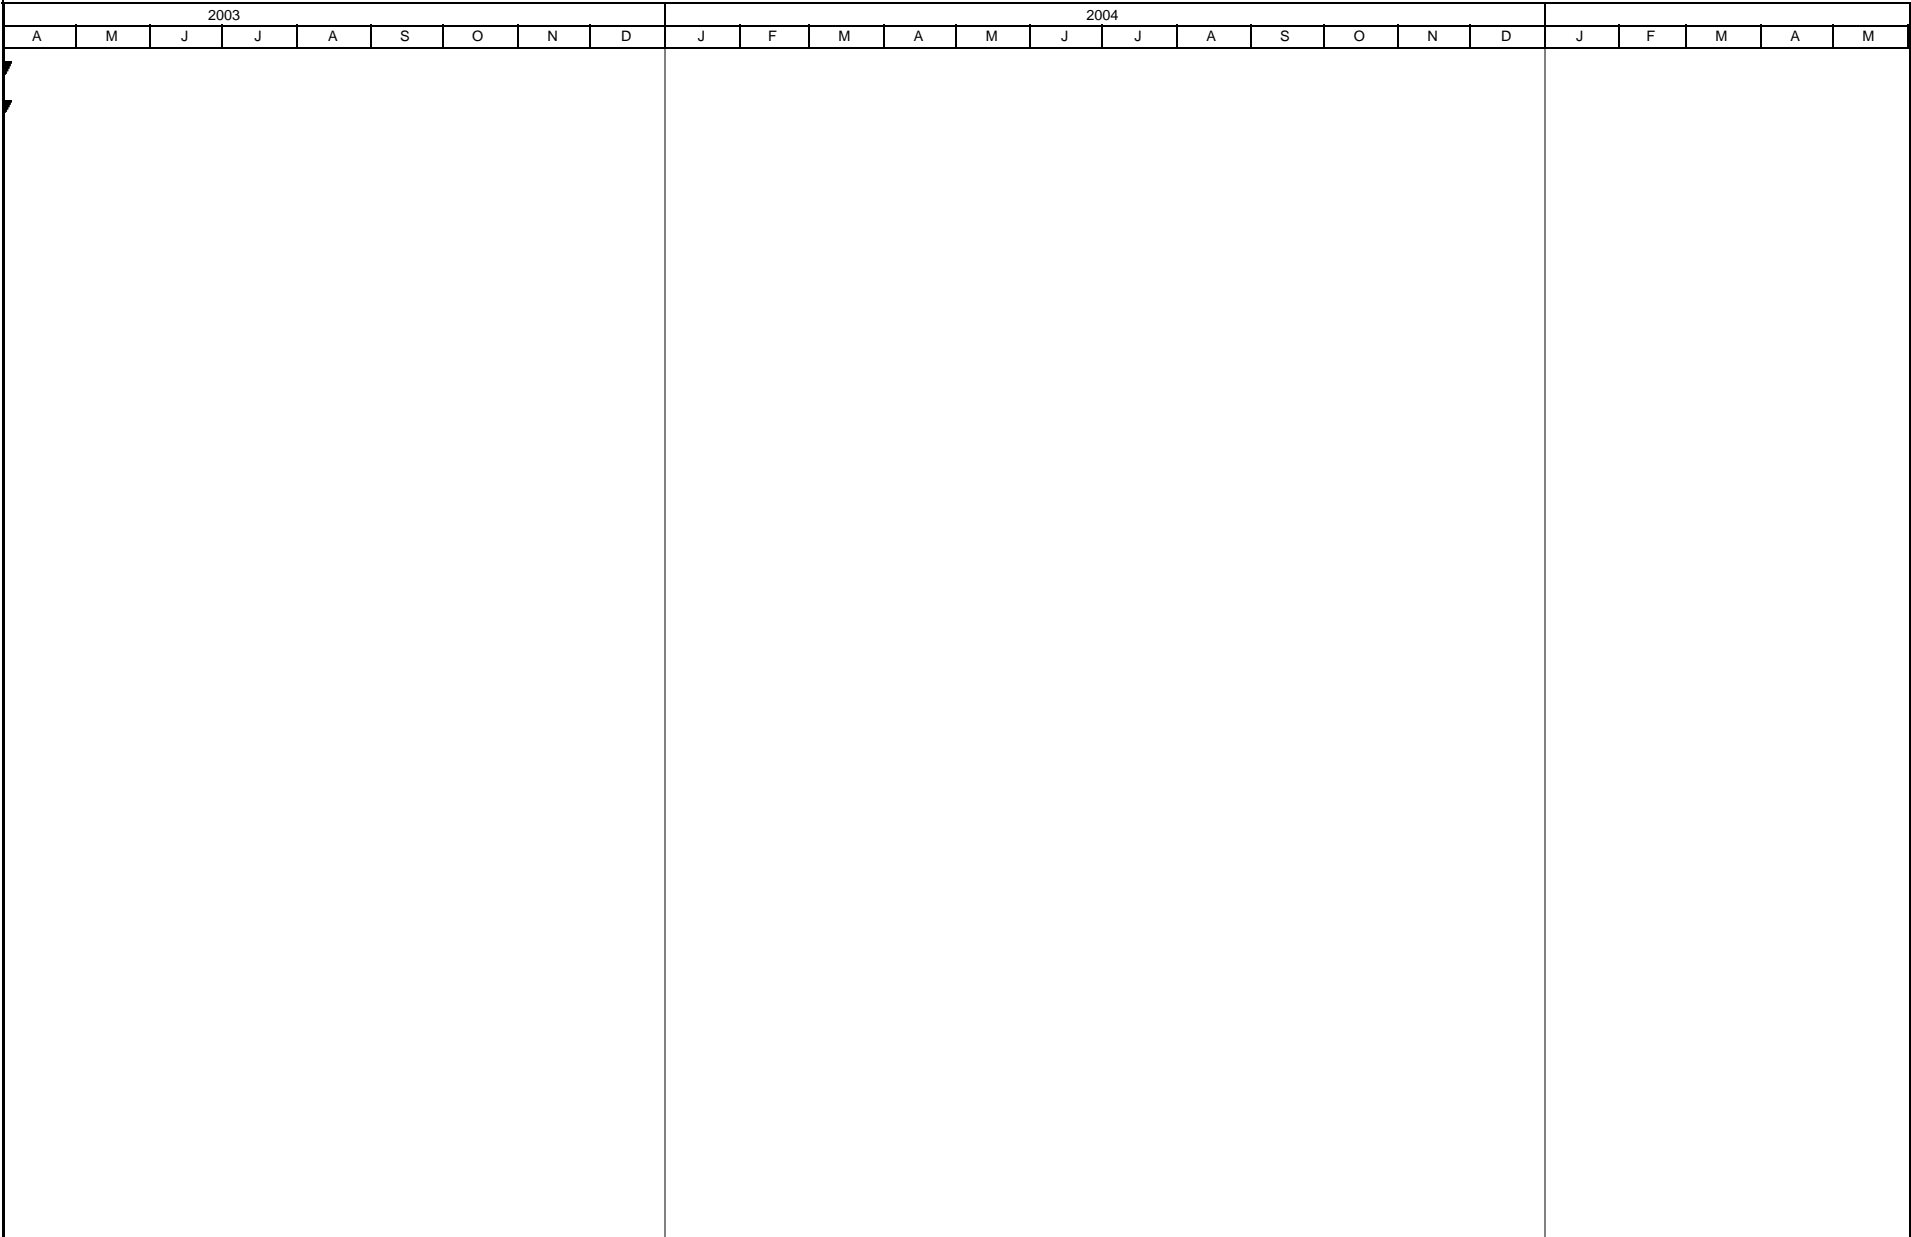

Milestones: <b>bold type</b> Summary Tasks: <u>underline</u>	Joint Task 	Summary (Joint) 	Progress 	Summ. Progress 
	Eur Task 	Summary (Eur) 	Milestone 	Split 
	US Task 	Summary (US) 	Completed Mlstrn 	

**ALMA Task Scheduling**  
Antenna Testing selected

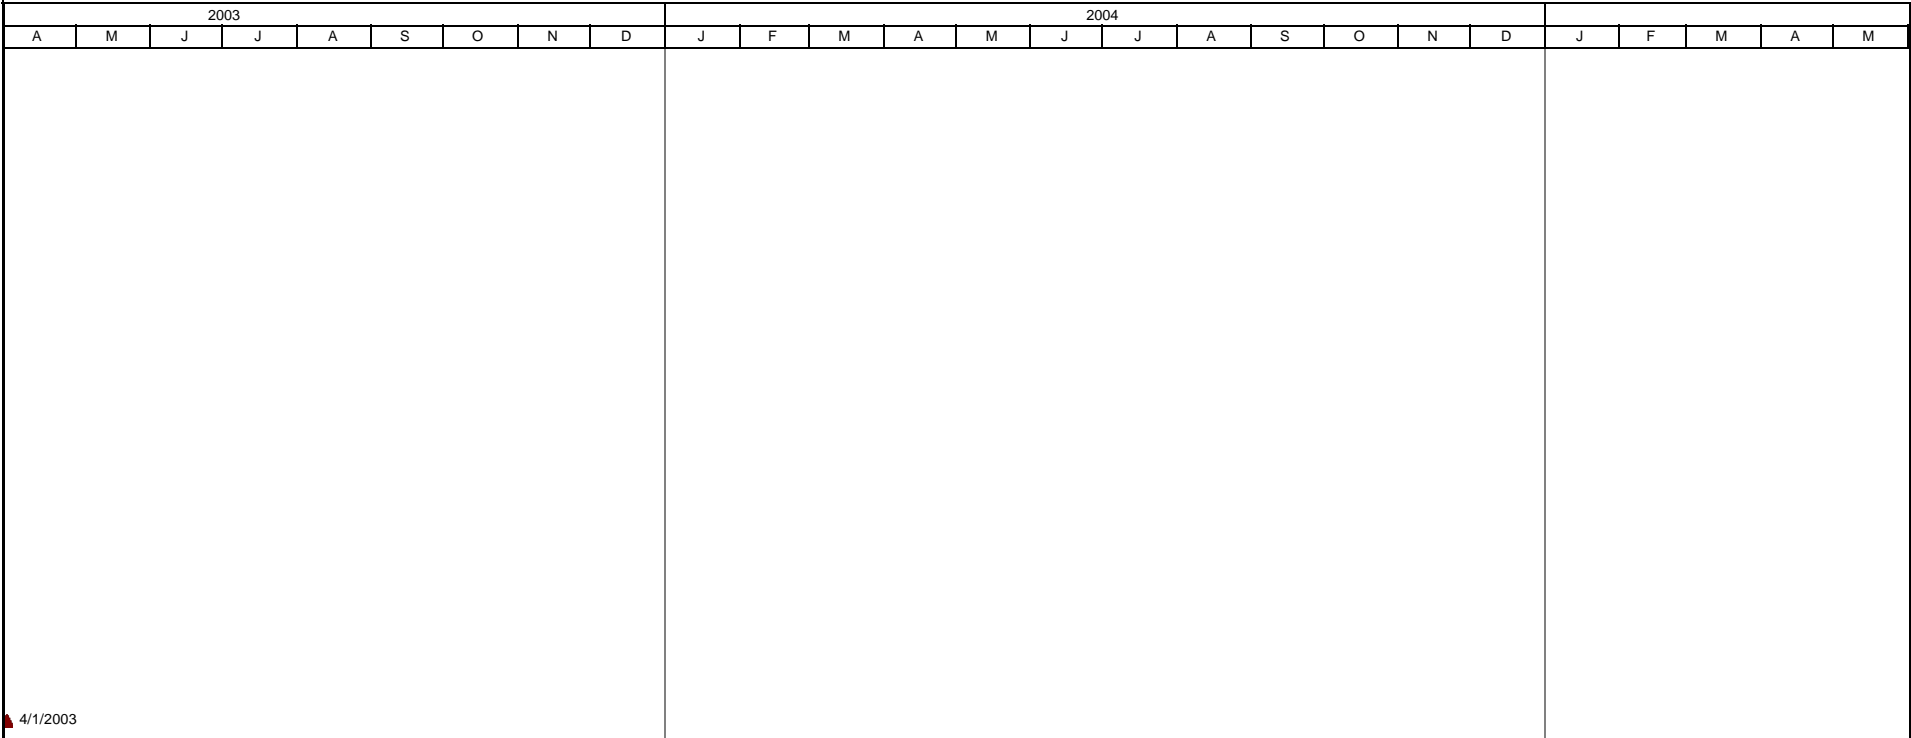

Milestones: **bold type**  
Summary Tasks: underline

Joint Task		Summary (Joint)		Progress		Summ. Progress	
Eur Task		Summary (Eur)		Milestone		Split	
US Task		Summary (US)		Completed Mlstr			
